



Topology

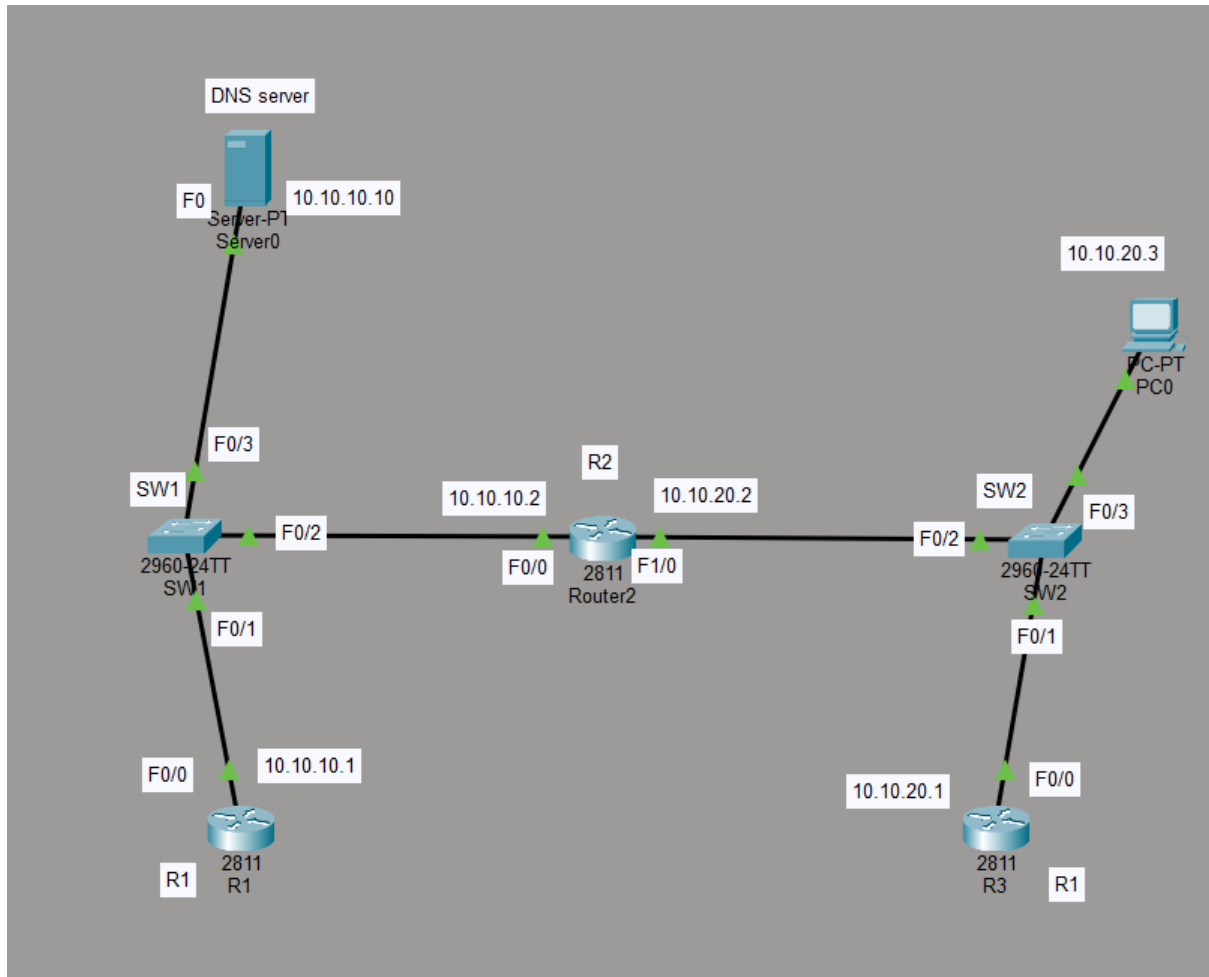

Step 22: attempt to reach DNS server from client device

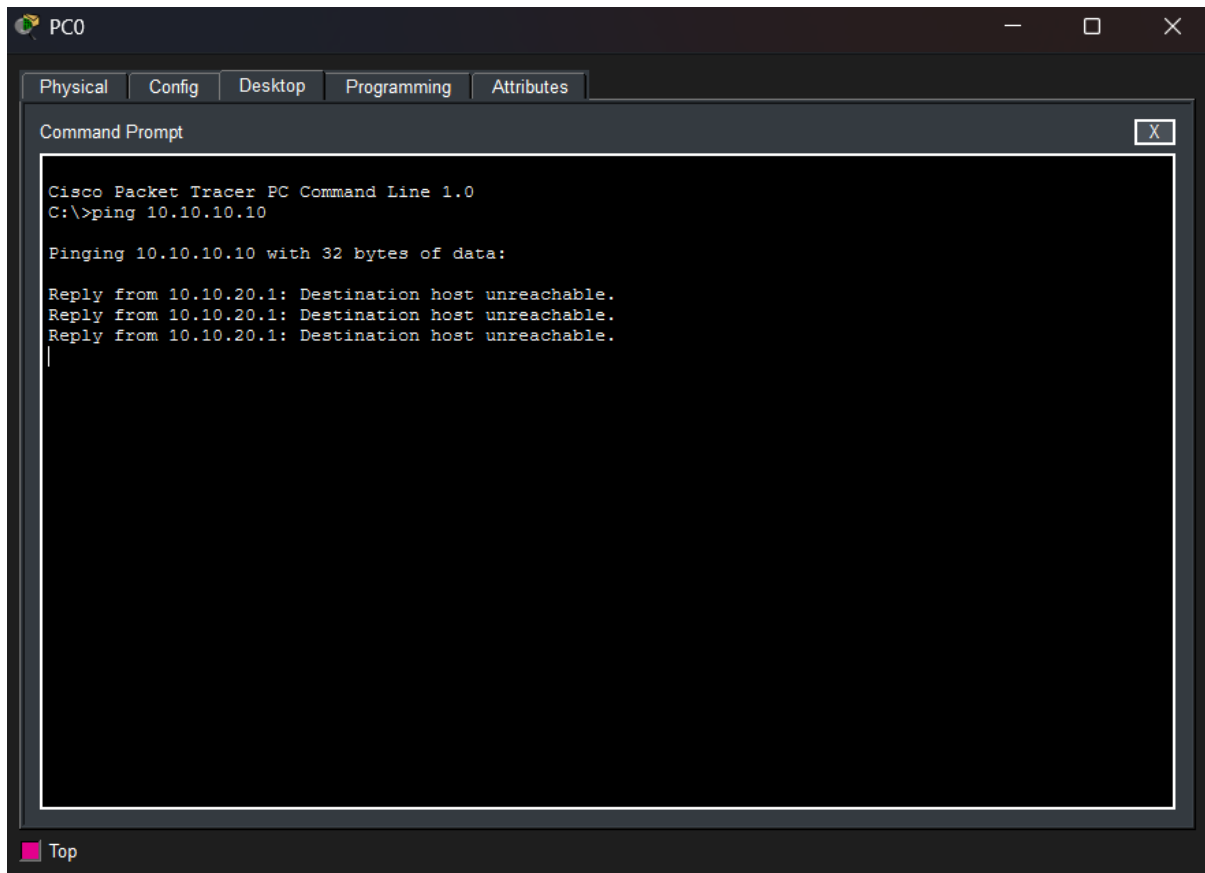

Could not reach the DNS server

23. Physical layer has no issues, everything is connected correctly.

Data link layer has no issues as frames are encapsulated and all normally.

Switch 2 to Router 3 has issues and gives a "Host unreachable" ICMP message, this is a layer 3 issue.

24. Router 3 has no static routing address anymore, this is the cause of connectivity failure.

25. Apply the command 'ip route 10.10.10.0 255.255.255.0 10.10.20.2' on router 3 CLI

26. Pc can ping DNS server properly

27. The layer 3 had an issue with connecting to the server. It was because of static routing being disabled. The evidence was that it would send host unreachable messages when going between switch 2 and Router 3

